



Standing Committee on Finance

10 September 2026

Forty-first meeting of the Standing Committee on Finance
23–25 September 2026
Sydney, Australia

I. Background paper on strategic planning for mandated reports of the Standing Committee on Finance in 2028

Expected actions by the Standing Committee on Finance

The Standing Committee on Finance will be invited to:

- a) Consider the draft workplan for delivering the mandated technical reports in 2028;
- b) Appoint co-facilitators to guide the work intersessionally on the preparations for the mandated technical reports.

II. Possible actions for consideration by the Standing Committee on Finance

1. Draft workplan for delivering mandated technical reports in 2028: The Standing Committee on Finance (SCF) may wish to consider the draft workplan presented in the Annex on the delivery of its mandated technical reports in 2028 and agree on a way forward.
2. Co-facilitators to guide work intersessionally: The SCF will be invited to appoint co-facilitators to guide the work on technical reports as follows:
 - (a) A pair of co-facilitators to guide the work on the third report on the determination of the needs of developing country Parties related to implementing the Convention and the Paris Agreement (NDR);
 - (b) A pair of co-facilitators to guide the work on the eighth biennial assessment and overview of climate finance flows (BA);
 - (c) A pair of co-facilitators to guide the work on the fourth report on progress towards achieving the goal of mobilizing jointly USD 100 billion per year to address the needs of developing countries in the context of meaningful mitigation actions and transparency on implementation (USD 100 billion progress report) and the second report on the doubling of adaptation finance;
 - (d) A pair of co-facilitators to guide the work on the first report on progress towards the new collective quantified goal on climate finance (NCQG progress report).

III. Background

3. COP 30 noted the workplan¹ of the Committee for 2026 and CMA 7 requested the Standing Committee on Finance to prepare a report on the doubling of adaptation finance in

¹ [Decision 1/CP.30](#), para. 2.

line with paragraph 18 of decision 1/CMA.3 for consideration at CMA 10 (November 2028), taking into account information in relevant UNFCCC reports and other relevant reports by other sources, as appropriate.²

4. Additionally, the SCF is mandated to produce the following technical reports by 2028:

(a) The first biennial report on collective progress towards all elements of decision 1/CMA.6 (NCQG progress report);³

(b) The eighth biennial assessment and overview of climate finance flows (BA), including a mapping of the available information relevant to Article 2, paragraph 1(c), of the Paris Agreement, including its reference to Article 9 thereof;⁴

(c) The fourth and final report on progress towards achieving the goal of mobilizing jointly USD 100 billion per year to address the needs of developing countries in the context of meaningful mitigation actions and transparency on implementation (USD 100 billion progress report);⁵

(d) The third report on the determination of needs of developing country Parties related to the implementation of the Convention and the Paris Agreement (NDR);⁶

5. At SCF 39, the Committee agreed on the updated SCF workplan in 2026 and to continue discussions on strategic planning of its mandated reports in 2026–2028. As requested at SCF 39, the SCF Co-Chairs prepared a note to provide suggestions on strategic planning for the delivery of technical reports mandated by 2028. The note was prepared on the basis of an in-depth review of existing practices and lessons learned, discussions during the SCF informal session prior to SCF 39, and a review by a communications expert from the secretariat of SCF technical products to enhance the visibility and accessibility of SCF outputs and to inform the strategic planning.

6. At SCF 40, the Committee discussed the note prepared by the Co-Chairs and provided feedback in relation to its overall framing and individual suggestions. In addition, five SCF members provided comments in writing on the Co-Chairs note. SCF 40 requested the Co-Chairs to prepare a joint workplan for delivering five technical reports, including indicative processes, timelines and outreach and engagement activities, as a proposal for consideration at SCF 41, based on comments at SCF 40 and written submissions.

7. The workload to deliver the mandated technical work in 2028 is unprecedented, both in terms of number of reports and their complexity. While the USD 100 billion progress report series and reporting on the doubling of adaptation finance are set to conclude in 2028 with the availability of climate finance data for 2025, subsequent reporting cycles for other mandated reports due on a biennial or quadrennial basis in 2030 and 2032 will continue to involve preparing complex technical reports with broad scopes.

8. In organising its work for the delivery of the mandated reports in 2028, the Committee has the opportunity to improve efficiencies for the simultaneous delivery of several technically complex outputs while meeting the expectations of target audiences such as Parties and non-Party stakeholders and ensuring outputs are of high quality and effective in informing discussions on climate finance.

² [Decision 5/CMA.7](#), para. 4.

³ [Decision 1/CMA.6](#), para. 30.

⁴ [Decisions 2/CP.17](#), para. 121(f) and [4/CP.24](#), paras. 4, 5 and 10.

⁵ [Decision 13/CP.27](#), para. 15.

⁶ [Decision 4/CP.24](#), para. 13.

Annex

Workplan for delivering mandated technical reports in 2028 [DRAFT]

I. Background

1. The SCF is mandated to prepare five technical reports in 2028 for consideration by COP 33 and CMA 10, including:

(a) The eighth biennial assessment and overview of climate finance flows (BA), including a mapping of the available information relevant to Article 2, paragraph 1(c), of the Paris Agreement, including its reference to Article 9 thereof;¹

(b) The third report on the determination of needs of developing country Parties related to the implementation of the Convention and the Paris Agreement (NDR);²

(c) The fourth and final report on progress towards achieving the goal of mobilizing jointly USD 100 billion per year to address the needs of developing countries in the context of meaningful mitigation actions and transparency on implementation (USD 100 billion progress report);³

(d) The second report on the doubling of adaptation finance in line with paragraph 18 of decision 1/CMA.3;⁴

(e) The first biennial report on collective progress towards all elements of decision 1/CMA.6 (NCQG progress report);⁵

2. This workplan is developed with a view to improve the efficiency of preparing technical work by the SCF and enhancing its communication impact.

3. The timeline, activities and outputs will be further elaborated as the appointed co-facilitators for each mandated report propose the objectives, scope and format of each report for consideration by the Committee at SCF 42 (2027) and subsequent meetings. The workplan does not prejudice the substantive content of the individual mandated reports.

II. Guiding principles

4. The following guiding principles are used as a basis for organising the delivery of the Committee's technical work:

(a) Ensure technical quality and effectiveness of outputs are data-driven and evidence-based;

(b) Ensure Committee ownership of key outputs to transmit to the COP and/or CMA;

(c) Ensure clarity in how stakeholders may engage with the work of the Committee;

(d) Ensure user-friendly outputs for wider dissemination and impact.

¹ [Decisions 2/CP.17](#), para. 121(f) and [4/CP.24](#), paras. 4, 5 and 10.

² [Decision 4/CP.24](#), para. 13.

³ [Decision 13/CP.27](#), para. 15.

⁴ [Decision 5/CMA.7](#), para. 4.


⁵ [Decision 1/CMA.6](#), para. 30.

III. Overall approach, roles and responsibilities

5. Building on the experience of the SCF in developing previous technical reports, the overall approach to organising the work is through three components comprising of *Committee-level work*, *technical-level work*, and *outreach and engagement* activities to engage relevant stakeholders in both the technical-level work and the committee-level work. SCF co-facilitators, Committee members, UNFCCC secretariat, technical authors and observers and stakeholders each have specific roles as the work is prepared through three general phases, as shown in figure 1. Activities and tasks under the three phases are further elaborated in detail under section V of the workplan.

Figure 1

Overall approach for the preparation of SCF technical reports

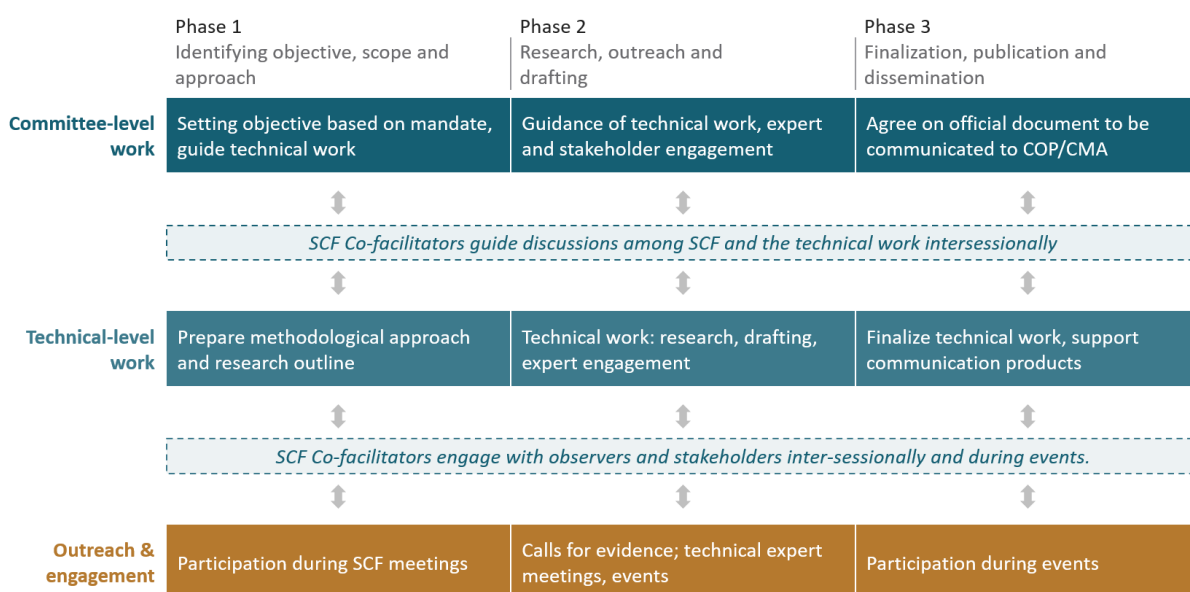

6. A pair of co-facilitators from the SCF, supported by the secretariat, have a central role in steering the technical-level and committee-level work, addressing guidance and feedback from SCF members, as appropriate, and engaging with observers and stakeholders during SCF meetings and relevant events.

7. The **Committee-level work** involves the work undertaken by the Committee members in deliberating, reviewing and guiding the work and agreeing on the output to be communicated to the COP and/or CMA in response to the mandate. In phase 1, Committee members review the mandate from the COP or CMA, identify the objective for the technical work and guide the preparation of the methodological approach and research outlines by the technical team. In phase 2, Committee members review the technical work and provide comments, discuss technical issues collaboratively and engage with observers and external experts through the SCF meetings or dedicated events. In phase 3, Committee members finalize and agree on the output to be communicated to the COP or CMA in response to the mandate, including any recommendations the Committee considers necessary for consideration by the COP and/or CMA. The document submitted to the COP and/or CMA constitutes the official output of the SCF in response to the mandate.

8. The **technical-level work** is undertaken by a team of technical authors including expert consultants supported by the UNFCCC secretariat. In phase 1, the technical team prepares a methodological approach and research outline under the guidance of the Committee. In phase 2, the work includes literature reviews, data and information gathering, engagements in technical expert meetings, and review of information submitted through calls for evidence. This work feeds into the drafting of technical work based on the research outlines guided by

the Committee. Co-facilitators may gather guidance and feedback on the technical level work from SCF members, before, during or after SCF meetings as needed, to ensure timely development of the report.

9. In accordance with established practice of the SCF, technical authors prepare the underlying technical work, under the guidance of the co-facilitators, while the official document to be communicated to the COP and/or CMA in response to the mandate is finalized and agreed by the SCF. In preparing underlying technical work, technical authors work to ensure the information presented is factual, respond and address comments and guidance received from Committee members with the guidance of co-facilitators.

10. As per current practice, the underlying technical work does not represent the views or opinions of the SCF or the UNFCCC secretariat and does not constitute an official text in any legal or technical sense (this disclaimer is included in final versions of underlying technical work).

11. ***Outreach and engagement activities*** are an important component of the technical preparation process, particularly for ensuring information on the most recent trends and developments are gathered as well as the perspectives of a broad range of stakeholders. In phase one, observers and stakeholders may participate in SCF meetings where the methodological approach and research outlines are deliberated. In phase 2, observers and stakeholders have an important role in responding to the calls for evidence and participating in technical expert meetings or SCF side-events to feed into the preparation of the reports and raise the Committee's awareness on the latest trends and developments in relation to climate finance (see section V on the approach to a single call for evidence across the five mandated reports in 2028). In phase 3, while the Committee finalizes the agreed products in response to its mandate, observers and stakeholders have an important role in participating in dissemination events.

IV. Expected outputs

12. In the course of preparing the technical work, the following outputs are expected to be delivered according to the information for consideration by the Committee to progress the work, information that is made available online through the SCF webpage, and the final communication products to support dissemination of the work.

13. **Outputs to progress the preparation of the work prior to SCF meetings** may include:

- (a) Draft methodological notes and research outlines specifying the objective, target audience, format and approach to the work;
- (b) Background papers and presentations for SCF meetings;
- (c) Drafts of the underlying technical work;
- (d) Drafts of the official output to be communicated to the COP and/or CMA;
- (e) Feedback sheets or documents outlining how guidance and comments received have been addressed or reflected.

14. **Outputs on the SCF webpage to support the preparation of technical work** and user-friendliness of the work may include:

- (a) Visibility of inputs received in response to the call for evidence;
- (b) Information on engagement activities such as technical expert meetings;
- (c) Descriptive catalogues of information such as on methodologies used to track climate finance, datasheets on latest climate finance trends from sources of information, and other annexes of information found in technical reports. This will enable the underlying

technical work to focus on key trends and findings with reference to the updated background material and catalogues of information online as needed;

15. **The final communication products and outputs** may include:

(a) The official SCF output to communicate to the COP and/or CMA in response to the mandate. This output will be an addendum to the annual SCF report to COP/CMA in the official UNFCCC document symbol in the UNFCCC document template format and adhering to UNFCCC style guide;

(b) A professionally designed version of the official SCF output to communicate to the COP and/or CMA;

(c) The underlying technical work consisting of long-form technical reports or technical background papers may be published in design or layout as needed.

(d) Datasheets on the figures and graphs in the underlying technical work and the annexes of the underlying technical work to improve dissemination and user-friendliness of the work;

(e) A 1–2 page factsheet on the key messages;

(f) Infographic(s) on the key messages.

V. Indicative timeline of activities

16. This section presents an indicative timeline of activities for delivering the five mandated reports in 2028. As noted in Table 1, the precise timing of activities and publications are subject to change based on the work of appointed co-facilitators for each report and the decisions by the SCF at SCF 42 and subsequent meetings.

17. In particular, scenarios for the publication of three of the five mandated reports are presented based on the discussions among SCF members during SCF 40 (summarised in paragraphs B.2.28–B.2.36 below). SCF 42 should aim to agree on the appropriate publication window for each mandated report in the context of considering the mandate and objective of each report and the delivery of a coherent package of technical work by the Committee.

A. Phase I – Identifying objective, scope and approach

18. The activities in this phase involve the consideration of the mandate and how the Committee decides to respond to the mandate in the scope and format of the technical work, taking account of other mandates under preparation and the coherence of its work.

19. **Appointment of co-facilitators:** At SCF 41, the SCF will be invited to appoint co-facilitators to guide the work on technical reports.

Table 1

Indicative timeline of activities for delivering SCF technical work by 2028

Activities and deliverables		2026	2027				2028			
		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Phase I: Identifying objective, scope and approach										
Appointment of co-facilitators										
Preparation of methodological notes outlining objective, scope, research questions, format and outputs for each mandated report			SCF42							
Development of annotated research outlines, methodological approach as applicable				SCF43	SCF44					
Phase II: Research, outreach and drafting										
Call for evidence: 3 rounds on specific themes/topics, deadlines 30 June 2027, 31 December 2027, 30 June 2028.				Rd1		Rd2		Rd3		
Technical expert meetings (tbc) in conjunction with SCF meetings			SCF42	SCF43			SCF45	SCF46		
3 rd NDR iterative drafts of technical work				ZOD	FOD		PFD	Publish		
Iterative drafts of technical work: 4 th USD 100bn progress report* 2 nd doubling adaptation finance report* 8 th BA*	Scenario 1: bring forward publication			ZOD	FOD		PFD	Publish		
	Scenario 2: late publication						ZOD	FOD	PFD/Publish	
1 st NCQG progress report							ZOD	FOD	PFD/Publish	
Phase III – Finalization, publication and dissemination										
Finalization of document editing, formatting and design										
Preparation of communications materials, web-based content and dissemination planning – one month before publication										
Communication and promotion of the reports including SCF side event at SBs and COP 33 and other events, continued into 2029										

Notes: ZOD=Zero-order draft; FOD=First-order draft; PFD=Pre-final draft. *The SCF would agree on timing of publication for each of these three reports at SCF42.

20. **Methodological notes:** For consideration at SCF 42, the co-facilitators for each mandated report, with the support of the technical team, will develop a proposed methodological approach and research outline for the report. The methodological note should include:

- (a) The proposed objective for the technical work, including the target audience, in order to inform the research outline and research questions;
- (b) Research outline for the technical work consisting of overarching chapters or components of the technical work and specific research questions to unpack the scope of the work;
- (c) Based on the research outline, a description of what is in scope and what is not in the scope of the technical work;
- (d) The proposed fit-for-purpose product format for the technical work that may include one of the models as described in figure 2;
- (e) A description of potential methodological considerations for approaching the underlying technical work. This could include the consideration of undertaking metadata analysis of existing work, as per the standard approach to the BA or USD 100 billion progress report; and/or to compile primary data and information from various sources to present, for example in the case of the NDR. The methodological considerations should unpack the potential ways of addressing research questions identified. For the successive iteration of a mandated report series e.g. the BA or the NDR, the note should describe the methodological practices for presenting data and information in the previous editions of the reports so that Committee members are fully aware of previous approaches and practices.

21. **Further methodological work and/or development of annotated outlines:** Following SCF 42, further work on the methodological approach for some mandated reports, particularly new mandates, may be necessary for consideration at SCF 43 and SCF 44. Further work could also include translation of research outlines into annotated outlines or zero-order drafts of technical work as appropriate.

Figure 2

Potential options for fit-for-purpose product formats for SCF technical work

	Standard model	Technical background papers and synthesis model	Policy brief model	Other models as proposed...
<i>SCF product to COP/CMA in response to mandate</i>	Executive summary of technical report Authors: Technical team, co-facilitators and SCF	Mandated report drawing from technical background papers Authors: Co-facilitators and SCF	Mandated report as short policy brief Authors: Technical team, co-facilitators and SCF	Tbd
<i>Underlying technical work</i>	Technical report Authors: Technical team of experts under guidance of SCF Co-facilitators	Technical background papers by topic e.g. access, impacts, effectiveness, innovations. Authors: Technical experts under guidance of SCF co-facilitators	Integrated in policy brief	Tbd

B. Phase II – Research, outreach and drafting

22. This phase involves data gathering, outreach and engagement with stakeholders to gather the latest metadata and information to respond to the research questions outlined in the research outline. This phase also includes the iterative drafting of the executive summary and technical report and presenting it for feedback at SCF meetings or intersessionally.

23. **Continuous literature review and data collection** by the technical team from sources of information as they become available. The team will engage with various stakeholders, including Parties, data providers, producers and aggregators to confirm interpretation and presentation of data. This work continues until the development of the pre-final draft of the report as relevant information becomes available.

1. Outreach activities

24. **Call for evidence:** A continuation of the previous practice where calls for evidence were launched for each technical report using the general outlines agreed by the Committee is likely to lead to confusing and overlapping submissions across reports. In order to ensure the submission of focused data and information on key research questions, in this cycle a **single call for evidence** will be launched, in consultation with all co-facilitators of the mandated reports. Furthermore, in order to ensure more timely submission of relevant information, the call for evidence will be in three stages with deadlines of 30 June 2027 for the first round of topics/research questions; 31 December 2027 for the second round of topics/research questions and 30 June 2028 for the final round of topics/research questions.

25. The initial round for the call for evidence could be launched at COP 31 during the SCF side event and revised following the decisions reached at SCF 42 on the timeline for preparing each report. An indicative sequencing of key topics and research questions could include:

(a) Round 1 launched at COP 31 and refined at SCF 42 with a deadline of 30 June 2027: Evidence related to improving access to climate finance/ methodologies and approaches for determining needs/ challenges and opportunities for determining needs;

(b) Round 2 launched after SCF 43 with a deadline of 31 December 2027: Evidence related to the effectiveness, impact and outcomes of climate finance flows/ identification of the needs of developing countries;

(c) Round 3 launched at COP 32 and refined at SCF 45: Evidence related to most recent climate finance data, trends and developments.

26. The visibility of submissions to the call for evidence will be improved with submissions posted on the SCF webpage by default unless the submitter does not agree. Following each round, an SCF news article could highlight the submission received and quotations from submitters on the rationale behind their submission.

27. **Technical expert meetings:** Further outreach through open technical expert sessions and stakeholder dialogues in conjunction with SCF meetings or webinars with broader stakeholder groups to gather inputs and views will be planned by the co-facilitators as needed, and in coordination with co-chairs, with space provided for submitters to the call for evidence to present their views. These meetings would provisionally be planned for taking place in conjunction with the first two SCF meetings of the year as the final meeting of the year prioritises the completion of work for the annual report to COP and the CMA.

2. Scenarios for timing of publications

28. **Iterative drafting and feedback:** The timeline for preparing the iterative drafts of each mandated report will be agreed at SCF 42 based on the consideration of the objective, scope and formats of the report as per the methodological notes. In consideration of strategic planning for delivering the five mandated reports in 2028 during SCF 40, members identified several scenarios or options for some of the reports. These are outlined below for each report in respect of their individual mandates and in order to inform discussions ahead of SCF 42 and do not prejudice substantive discussions on the reports. A choice of scenarios may apply for each report based on its own mandate and requirements.

29. **Third needs determination report:** The SCF could aim to publish the 3rd NDR in early Q2 of 2028. The preparation of the technical work could be as follows:

(a) A zero-order draft of the underlying technical work would be prepared for consideration at SCF 43 (Q2 2027) based on the research outline agreed at SCF 42 (Q1 2027);

(b) A first-order draft of the underlying technical work would be prepared for consideration at SCF 44 (Q3 2027) based on guidance and comments received at SCF 43 and in written form. In addition, an initial draft of the official SCF output to be communicated to COP and CMA would be presented for feedback;

(c) The data cut-off for information on needs to be included in the 3rd NDR would be set at 31 December 2027;

(d) A pre-final draft of the underlying technical work and official output would be prepared for consideration at SCF 45 (Q1 2028), and the Committee would finalize and agree on the official output to be communicated to the COP and CMA at SCF 45;

(e) In parallel to drafting the pre-final drafts of the executive summary and the technical report, the professional editing and graphic design will be prepared to ensure the report is ready for publication as soon as possible after SCF 45.

30. **Fourth USD 100 billion progress report:** In discussions during SCF 39 and 40, two scenarios were identified for preparing the fourth USD 100 billion progress report. *Scenario 1* involves bringing forward the publication of the report to early 2028. Some members suggested to bring forward the publication to 2027, however the current mandate to the SCF is to produce biennial reports starting in 2022, and therefore the fourth report may only be delivered in 2028. Bringing forward the publication to early 2028 is facilitated by the need to only collect one year of preliminary data (2025) to complete the reporting on progress towards the USD 100 billion goal by 2020 through 2025. This scenario would involve the collection of preliminary data by the SCF from Parties on climate finance provided, mobilized and received in 2025, during 2027. The drafting of iterative zero-order, first-order and pre-final drafts of technical work would follow the same timeline as the 3rd NDR.

31. *Scenario 2* involves continuing the current timing of publication with view to publishing the report after SCF 47 in Q3 2028. This scenario would avail of official data on climate finance provided and mobilized in the years 2025 and 2026 in BTR3s submitted in response to the invitation in decision 1/CMA.6, para. 31, by 30 June 2028. In this scenario:

(a) A zero-order draft of the underlying technical work would be prepared for consideration at SCF 45 (Q1 2028) based on the research outline agreed and developed in 2027;

(b) A first-order draft of the underlying technical work would be prepared for consideration at SCF 46 (Q2 2028) based on guidance and comments received at SCF 45 and in written form. In addition, an initial draft of the official SCF output to be communicated to COP and CMA would be prepared for consideration at SCF 46;

(c) A pre-final draft of the underlying technical work and official output would be prepared for consideration at SCF 47 (Q3 2028), and the Committee would finalize and agree on the official output to be communicated to the COP and CMA at SCF 47;

(d) In parallel to drafting the pre-final drafts of the executive summary and the technical report, the professional editing and graphic design will be prepared to ensure the report is ready for publication as soon as possible after SCF 47.

32. **Second doubling of adaptation finance report:** As per discussions during SCF 39 and SCF 40, the considerations for timing of publishing the second report on the doubling of adaptation finance are similar to the fourth USD 100 billion progress report given that the doubling is urged to be achieved by 2025. Therefore, the same scenarios apply as outlined above in paragraphs 30-31.

33. **Eighth BA:** In discussions held during SCF 39 and SCF 40, the scenario of bringing forward the publication of the eighth BA to early 2028 or continuing the current publication

window just ahead of COP was mentioned. *Scenario 1* (early 2028 publication) would involve the same timeline of iterative drafting as the 3rd NDR.

34. *Scenario 2* involves the same timeline as identified in the fourth USD 100 billion progress report (paragraph 313131).

35. **First NCQG progress report:** Given this is the first time the SCF is preparing a report on progress on the NCQG, and the comprehensive nature of the mandate to report on collective progress towards all elements of decision 1/CMA.6, sufficient time will need to be allocated for deliberation on the methodological approach and drafting.

36. While details will be proposed by appointed co-facilitators ahead of SCF 42, it is proposed that continued methodological work is discussed in 2027 with a view to developing zero-order drafts by SCF 45 (Q1 2028), a first-order draft by SCF 46 (Q2 2028) and a pre-final draft by SCF 47 (Q3 2028) with finalization and publication as soon as possible thereafter.

C. Phase III – Finalization, publication and dissemination

37. This phase finalizes the documents for publication and the supporting materials for dissemination. The key steps include:

(a) Following finalization of the official SCF products to communicate to COP and CMA, the unedited, undesigned and unformatted outcome drafts will be made available on the SCF website;

(b) In line with UN publication processes, the official SCF product will undergo a final round of editing based on the agreed text. Following editing:

(i) The official document template, with document symbol, will be contained in an addendum to the SCF annual report to the COP and CMA;

(ii) The official SCF product will be professionally designed and layout for publication will be made available on the SCF website as soon as possible after the final editing process;

(iii) The relevant underlying technical work will be professionally designed and layout subject to budget;

(c) In addition to the documents, an infographic of key messages will be designed and published on the SCF website following SCF 47;

(d) The dedicated webpage on the SCF website will include the documents, infographics, and additional materials such as online annexes and graph data in accessible forms to increase user-friendliness of the information in the report;

38. Following finalization of the report, the key findings will be disseminated through:

(a) Press release from the SCF and UNFCCC, including through social media channels;

(b) Events to launch the report will include a SCF side event at SBs and COPs and other speaking opportunities or participation in related events on climate finance that may also occur in 2028 and 2029.

39. Dissemination packs for SCF members will include a presentation slide deck on the content of the work, talking points and social media quotes will be prepared for SCF members for their potential use in their capacity as members of the committee and participation in various events.
